



# ARRA FHWA Award 0025065

As of 12/14/2014

Award Date: **4/23/2009**

[Click for 1512 Report](#)

ARRA Type: **MDOT**

Project Status: **Fully Completed**

Project Name: **US 45 FM JUST N OF DRYDEN RD TO THE LEE CL**

Award Description: **Highway Infrastructure Investment Grants**

Project Description: **This project will resurface and extend the life of the pavement for approximately 8 miles on US Highway 45 between New Wren and the Lee County Line, Monroe county.**

Infrastructure Rationale: **4R Resurfacing. Preserve/Create jobs; and economic recovery. Invest in transportation.**

Award Amount: **\$3,508,915.00**

Jobs Creation To Date: **29.09**

Total Federal ARRA Received: **\$3,508,915.00**

Location: **Nettleton 38858**

Total Federal ARRA Expenditure: **\$3,508,915.00**

## VENDOR PAYMENTS

Vendor Name: **{ name not entered }**

DUNS: **039428339**

Payment: **\$3,343,733.00**

Service Description: **Overlaying approximately 8 miles of US Highway 45 between New Wren and the Lee County Line**

## MDOT PROJECTS

Project Number: **105463-301000**

Responsible Agency: **MDOT**

Location: **District 1, Monroe County**

Route: **45**

Plan Begin: **5/1/2009**

Total Estimated Cost: **\$3,522,545.92**

Plan End: **4/24/2010**


Project Let: **5/26/2009**

Total Expended: **\$3,522,545.92**

Termini: **\*\*US 45 FM JUST N OF DRYDEN RD TO THE LEE CL**



# PROJECT MAP

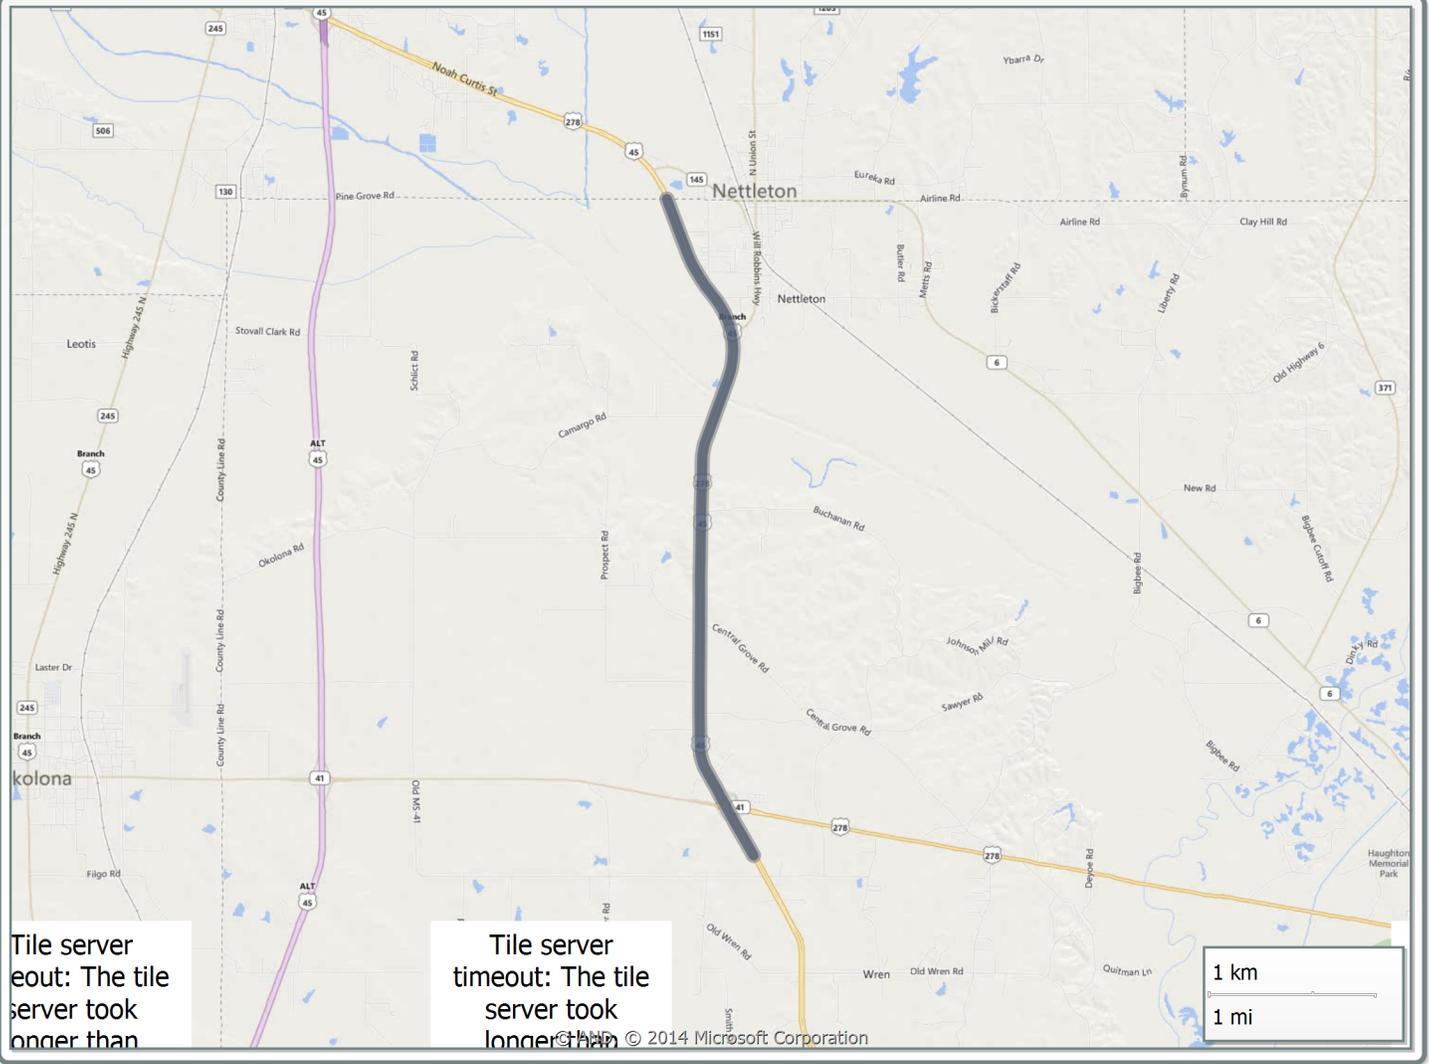

Tile server timeout: The tile server took longer than

Tile server timeout: The tile server took longer than

